



# City of Eagle Point


Robert Miller, Public Works Director/City Engineer

## Public Works Update – Stevens Road Improvements

August 29, 2019

### East Main Street/Stevens Road Improvements

Construction continues for Stage 1 of the E. Main Street/ Stevens Road Improvements by Knife River Materials. Stage 1 will be closed for construction into October of 2019. Access is limited to residents only and to emergency vehicles at all times. A temporary pedestrian detour was placed on Onyx Road, and accessed from Tabor Avenue and Bridgeport Drive on each side.

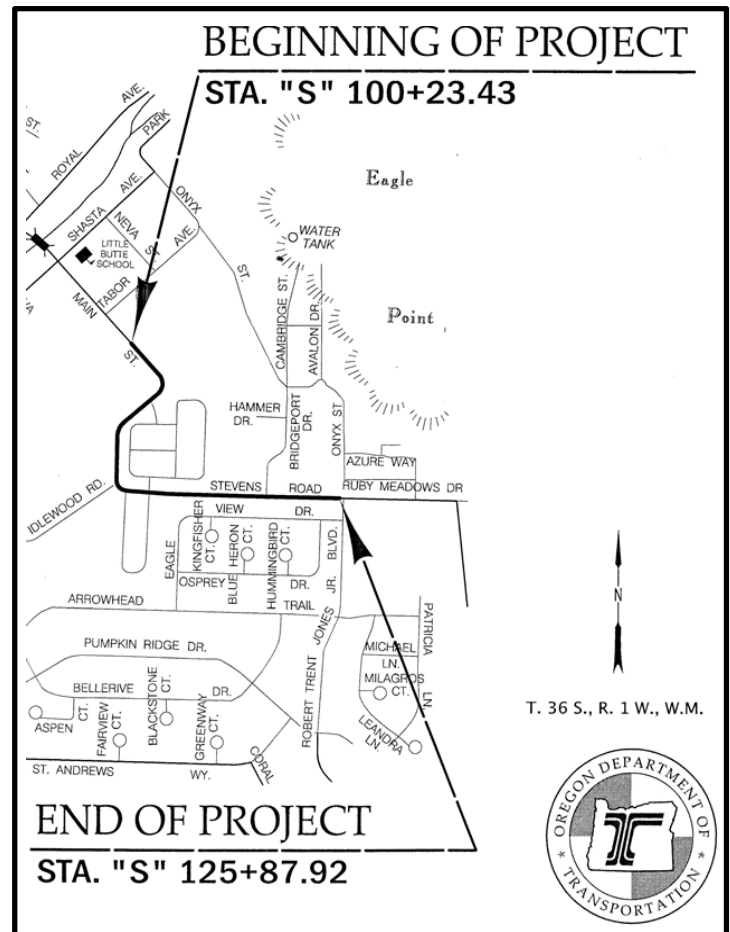

Stage 1 Retaining Wall Construction



Retaining Wall "B" Construction.



The Ultrablocks were delivered to the site, and unloaded directly by Knife River Materials on Main Street. This saved time and effort for both the City and Knife River.



Stage 1 pavement removed.



Relocation of the RVSS manhole continues.



Onyx Road temporary pedestrian detour.

### Two Week Look Ahead

Utility relocation of City water service lines and hydrants will continue through the first week of September. Installation of the retaining Wall “B” is scheduled to be completed. The storm system for Stage 1 is scheduled to be completed, with the storm system in Stage 2 scheduled to begin. Stage 2 extends from Idlewood Drive to Robert Trent Jones Boulevard.

### Public Outreach

Regular updates continue to be sent to the email notification list, and placed on the City’s website. Steve Sparkman, Construction Project Manager for OBEC Consulting Engineers, is available to meet onsite with property owners who have specific questions about the project construction.

For project updates please see the City of Eagle Point website, [www.cityofeaglepoint.org](http://www.cityofeaglepoint.org). For general questions, or to be placed on the email notification list for updates please contact Brigitte at City Hall, (541) 826-4212, [brigitte@cityofeaglepoint.org](mailto:brigitte@cityofeaglepoint.org).

