



# City of Eagle Point


**Public Works Update – E. Main Street/Stevens Road**  
August 14, 2019

## East Main Street/Stevens Road Improvements

Construction continues for Stage 1 of the E. Main Street/ Stevens Road Improvements by Knife River Materials. Stage 1 will be closed for construction through September of 2019. Access is limited to residents only and to emergency vehicles at all times. A temporary pedestrian detour was placed on Onyx Road.



Excavation for Wall “B”.

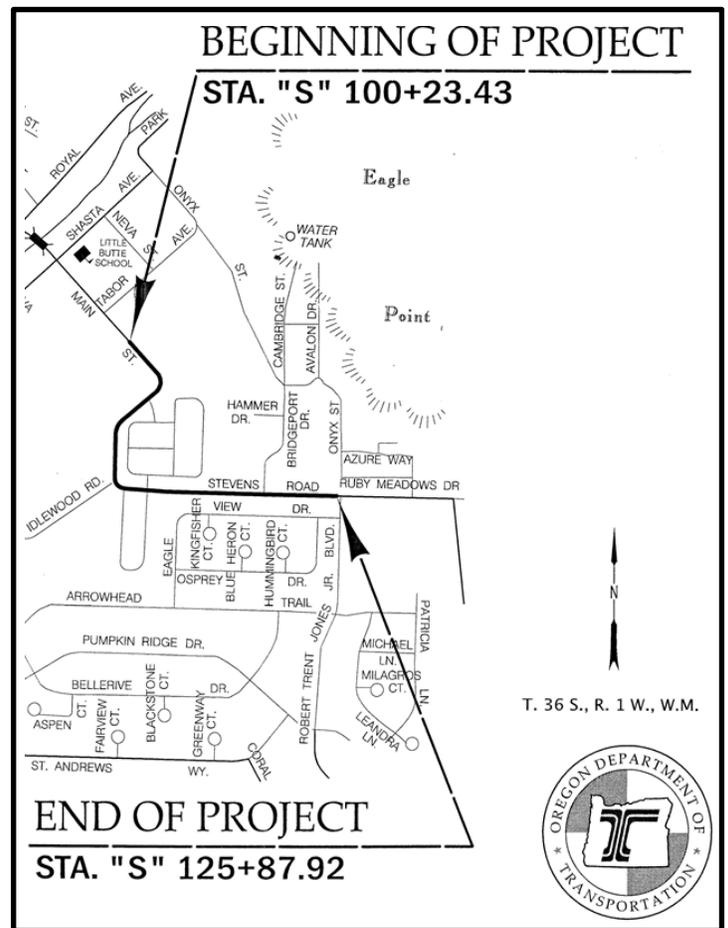



Installation of the Ultrablocks for Wall "A" was completed.



Ultrablock Wall "C" installation.

The Ultrablocks were delivered to the site, and unloaded directly by Knife River Materials on Main Street. This saved time and effort for both the City and Knife River.



Storm pipe materials delivered on site.



Utility relocation continued.



Onyx Road temporary pedestrian detour.

### Two Week Look Ahead

Utility relocation of City water service lines will continue over the next two weeks. Construction of the new storm system for Stage 1 is scheduled to begin August 14, 2019. Installation of the Ultrablocks for Wall “B” are scheduled to begin August 15, 2019. Relocation/modification of an RVSS manhole will allow completion of Wall “B.”

### Public Outreach

Regular updates continue to be sent to the email notification list, and placed on the City’s website. Steve Sparkman, Construction Project Manager for OBEC Consulting Engineers, is available to meet onsite with property owners who have specific questions about the project construction.

For project updates please see the City of Eagle Point website, [www.cityofeaglepoint.org](http://www.cityofeaglepoint.org). For general questions, or to be placed on the email notification list for updates please contact Brigitte at City Hall, (541) 826-4212, [brigitte@cityofeaglepoint.org](mailto:brigitte@cityofeaglepoint.org).



The Oregon Department of Transportation (ODOT) grant funded project will construct 6-foot bikes lanes, sidewalks, decorative lighting, and a new storm system from Robert Trent Jones Boulevard to Hillside Elementary School on the south side, and from Bridgeport Drive to Hillside Elementary on the north side. Knife River Materials is the main contractor, with OBEC Consulting Engineers providing construction management for ODOT/City of Eagle Point. The City received over \$2.8 million towards the estimated \$3.8 million project.
